Fondation Eagle

Report Form

Interim or Final report: Final

Donor name: Fondation Eagle

Fondation Eagle reference: FF725

Name of Charity: Mondo Foundation

<u>Introduction:</u> Enabling quality education for local children in the village of Lenjani by facilitating the completion of a half-built primary school.

Date of grant accepted: 29th November 2024

Amount: £26,687

<u>Conversion rate, date & amount in local currency:</u> Conversion is GBP to TZS, conversion rate correct as of 16.07.24. Conversion rate is 1 GBP = 3,453 TZS

<u>Name and exact location of the project:</u> Schools Completion. The village of Lenjani (population 2,300), a plateau area in the Lemanyata ward of Arusha Rural District.

Period of Project: 6 months, January 2025—June 2025

Project beneficiaries: We supported 601 children to access primary education.


<u>Details of the project:</u> Previously, the young children of Lenjani village were required to walk 5-8km per day to the nearest primary school in the village of Olkokola. This tiring and physically demanding journey resulted in many children dropping out of education before the last year of primary school (age 13). Now teachers are seeing a huge demand for spaces at the school, and it is anticipated that the school will be over-subscribed as early as 2026. We registered 601 new students (318 boys and 283 girls).

Three classrooms had been started prior to the project commencing and these were finished with the addition of floors, windows, paint and desks, allowing space for 150 children to receive their education. Two new classrooms which had been planned but not started, were also completed in the above timeframe with room for 100 children.







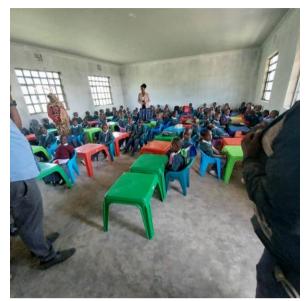

A half-finished staff office was also completed with flooring, paint and furniture. As well as this, essential plumbing work was undertaken on the toilets meaning children now have access to sanitation facilities as well as clean water and no longer have to bring their own water from home.





Detailed budgets and actual expenditure summary and comparison:

<u>Expenditure</u>	Cost (UK)	Cost (TZS)	Spent (UK)	Spent (TZS)	Leftover		
<u>Lenjani expenditure - classrooms</u>							
Concrete works	£696.00	2,400,000	£696.00	2,400,000			
Roof coverings and structure	£4,479.78	15,447,500	£4,479.78	15,447,500			
Ceilings	£2,886.81	9,954,500	£2,886.81	9,954,500			
Doors	£362.50	1,250,000	£362.50	1,250,000			
Windows	£1,993.75	6,875,000	£1,993.75	6,875,000			
Floors and finishings	£4,554.09	15,703,750	£4,554.09	15,703,750			
Painting and decoration	£1,149.63	3,964,250	£1,149.63	3,964,250			
Electrical installation	£942.50	3,250,000	£942.50	3,250,000			
Labour charge	£5,119.36	17,652,975	£5,119.36	17,652,975			
Subtotal	£22,184.42	76,497,275	£22,184.42	76,497,275	£0.00		
<u>Lenjani expenditure - office</u>							
Timber, iron and nails	£389.47	1,343,000	£389.47	1,343,000			
Cement and sand	£268.25	925,000	£268.25	925,000			
Walls and tiling	£307.11	1,059,000	£307.11	1,059,000			
Table and chairs	£580.00	2,000,000	£580.00	2,000,000			
Windows and grills	£209.38	722,000	£209.38	722,000			

Brushes	£3.77	13,000	£3.77	13,000			
Transport	£29.00	100,000	£29.00	100,000			
Labour charge	£290.00	1,000,000	£290.00	1,000,000			
Subtotal	£2,076.98	7,162,000	£2,076.98	<u>7,162,000</u>	£0.00		
Lenjani expenditure – WASH facilities							
Structure	£492.59	1,698,600	£492.59	1,698,600			
Superstructure	£518.33	1,787,350	£518.33	1,787,350			
Roofing	£288.26	994,000	£288.26	994,000			
Finishing works	£363.23	1,252,500	£363.23	1,252,500			
Painting and decoration	£41.18	142,000	£41.18	142,000			
Plumbing and engineering	£643.80	2,220,000	£643.80	2,220,000			
Labour	£435.00	1,500,000	£435.00	1,500,000			
Transport	£29.00	100,000	£29.00	100,000			
Subtotal	£2,811.39	9,694,450	£2,811.39	9,694,450	£0.00		
Subtotal	£27,072.79	_		_			
Contribution from Mondo	-£385.79						
Total	£26,687						

Results:

Before grant	After grant		
There were two classrooms already completed	There are seven classrooms in total		
There were three classrooms with a roof but	There are seven classrooms in total		
no floors, desks, paint or windows			
There were two classrooms not started	There are seven classrooms in total		
There was an office with a roof but no floor,	There is a completed office		
chair or paint			
There were incomplete toilets – students	There are completed toilets		
brought water from home as the plumbing			
facilities were incomplete			
There was a completed kitchen where children	There is a completed kitchen where children		
make porridge	make porridge		

Follow up: Erneth, (Area Co-Ordinator), will work alongisde Mondo Volunteers and villagers from Lenjani to conduct research into the difference made by the provision of the primary school. They will collect data surrounding the number of children completing primary education, with studies conducted to gain a deeper insight into the gender gap and how female students specifically are benefitting from the new opportunities. After the first year, the initial cohort of students will be asked questions about their feelings towards education, their motivations for continuing studying, and whether having access to a local school has had an impact on their ability to attend classes, as well as their overall grades, and their aspirations for the future.

<u>Conclusion</u>: The completion of this primary school will be lifechanging for the children of Lenjani now and for years to come, and we thank Fondation Eagle for making this possible. Primary school dropout rates in Tanzania are estimated to be around 17%, therefore the provision of easy to access

education- particularly in rural areas such as Lenjani- is crucial. With the financial support provided by Fondation Eagle, more children than ever can remain in school for longer and reach their full potential.

Signature and date: R. Parkinson, 28th June 2025
